

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, March 25, 2014
10:00am




Present

The following is a summary of the discussions held during our progress meeting of the above date. The meeting was held at approximately 10 am in the Council Chamber at City Hall. The following agenda was generally followed. A sign in sheet was passed around and those present signed in. A copy of said sign-in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)

4. Expected work this next period
5. Questions
6. City's comments
7. Business/Property Owner comments
8. Field Review as needed
9. Wrap Up

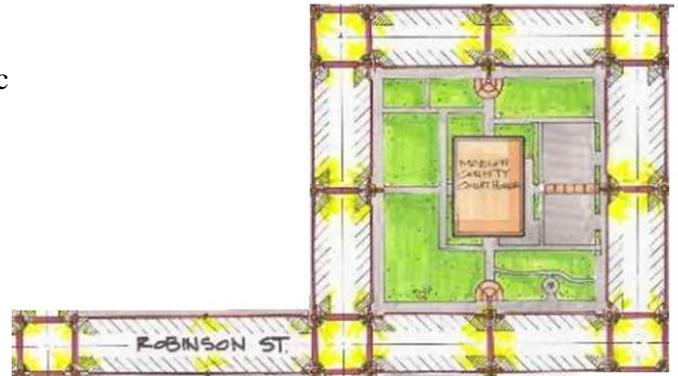

Work to date

Based on response of the County and information to date, work will progress to the 3rd St section next as per plans.

County project should be done by July 1 minimizing the overlap and coordination needed.

Only 1 lateral sewer service remains. All vaults and water services are completed. Subgrade and subdrains will start immediately. Water main work at the intersection will be done tonight.

Paving should start late next week. TK Concrete will not be on site until May 1 to start 2nd St.

2 double services for sanitary were installed.

Staking for the Robinson intersection is scheduled for Thursday.

V&K will check if planter arms can handle 60 lbs.

A meeting will be needed to discuss walk adjustments for the County. This needs to occur asap.

HP is thinking that they may be paving the mainline of the street by month's end, weather

depending.

An RFI was submitted by VME. The request was for location of the speaker wiring entering City Hall. This was previously discussed. The City wants this to enter on the west face of the building just south of the first window (lower level), 6 inches (+/-) below the top of the window.

The next meeting is slated for Monday, May 5 at 10 am
