

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, May 20, 2014
10:00am (Knoxville Public Library)




Present

The following is a summary of the discussions held during our progress meeting of the above date. The following agenda was generally followed. A sign in sheet was passed around and those present signed in. A copy of said sign-in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)
4. Expected work this next period
5. Questions
6. City's comments
7. Business/Property Owner comments
8. Field Review as needed
9. Wrap Up

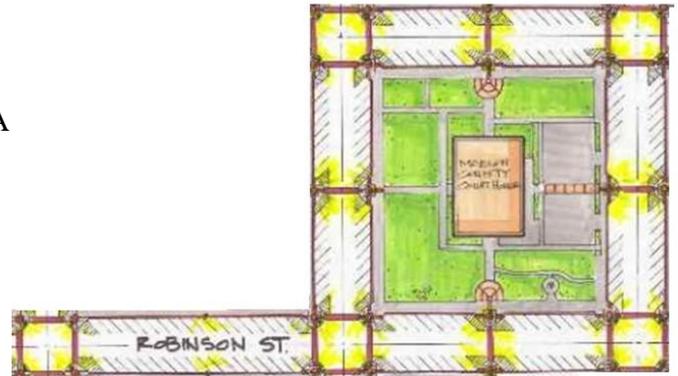

Work Completed to Date

Marion County clock tower project is on track for expected end of June completion. Minimal disruption is expected at this point.

6" PCC walk will be used at the crossing on the Court House side.

Mainline and south parking of Robinson Street is in place. Bump out forming is started. TK Concrete is now on site. Crosswalks on Third Street are getting started as well.

Parking and walk completion is next for TK Concrete on Second Street.

Following discussions, it was decided that Farmers Market could move north and stay on the square while Hawkeye Paving completes work so progress is not delayed.

Van Maanen Electric will be on site over the next 2 weeks placing conduit and footings.

Hawkeye Paving is trying to place as much PCC (concrete) in the next 2 weeks to stay on schedule for moving onto Third Street by/around June 1.

Discussion took place on footings. As detailed, the footing must be above walk grades up to 1.5 inches above, max.

Paver installation has not started. Hawkeye Paving is calling to get them on site.

Iowa State Savings Bank decided against heated walks, so Hawkeye Paving will continue with normal walk construction there.

Sealing of Second and Robinson Streets needs to occur ASAP.

Pay Estimate will be prepared and processed for all work completed by May 23rd.

Stop signs have been selected and need to be ordered.

The next meeting is scheduled for **10:00a on Tuesday June 3rd.**
