

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, October 1, 2013
10:00am




Present

The following is a summary of the discussions held during our progress meeting of the above date. The meeting was held at approximately 10 am in t following agenda was generally followed. A sign in she signed in. A copy of said sign in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)
4. Expected work this next period
5. Shop drawings
6. Questions
7. City's comments
8. Business/Property Owner comments
9. Field Review as needed
10. Wrap Up

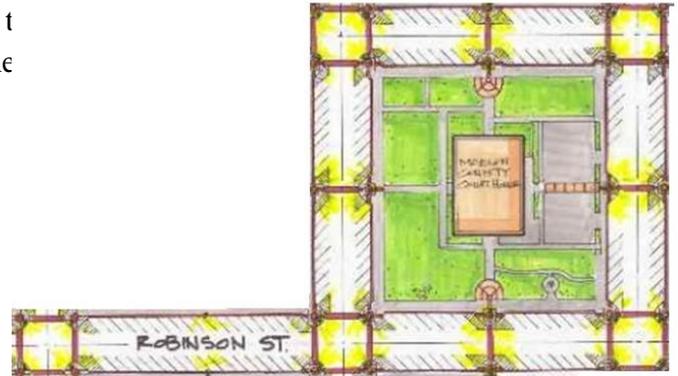

Work to date (since last meeting). Contractor has continued on underground work on Second Street. Many if not all the services are 2 lines from the building out to a point and merge together into one outside the foundation wall. The cast pipe is broke many times and requires repair. Some cases have gone inside the building for repair. It is expected that storm and sanitary work will be completed by end of next week, dependent upon weather. Water main work in the intersection will follow and may require Saturday work to maintain water flow.

Expected work this period. Paving crews will arrive October 21 with prep and paving to follow. Hawkeye will pave the mainline and TK will perform hand-pours. The current thinking and expectation is that this stage will be completed by mid to late November. Contingency plans are in place for the Living Windows event. West side sidewalks will be poured first.

Closing of Second Street from Robinson Street south to the alley will begin the week of October 7th – 11th. Parking adjustments will be needed and the work will be completed in approx. three weeks.

Temporary ponding of water following rain events may be experienced due to transition grades when new meets old pavements. This will only occur until the additional project blocks are replaced to match the new street grades.

The City of Knoxville is not requiring permits for plumbing work if it is associated with repair of the service. Permits are required for new services and/or new construction.

Taso's new services are located in the field. Hawkeye will be installing these services this week.

A layout for the new water main work at the intersection was distributed at the meeting. Some water interruptions will likely be experienced. FYI, the dental office is closed Thursdays afternoon and work on their water service will be scheduled around office hours as much as is feasible and possible.

Videotaping of the new sewers will occur next week, late.

A discussion on hydrants took place and the supplied hydrant will be installed.

A temporary storm connection will be made in the NE corner of the intersection to convey storm water from the east during construction.

Some new utility pole parts are being delivered to the contractor. Old signals should be removed next week.

The next meeting is scheduled for October 15th at 10 am.
