

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, March 25, 2014
10:00am




Present

The following is a summary of the discussions held during our progress meeting of the above date. The meeting was held at approximately 10 am in the Council Chamber at City Hall. The following agenda was generally followed. A sign in sheet was passed around and those present signed in. A copy of said sign-in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)

4. Expected work this next period
5. Questions
6. City's comments
7. Business/Property Owner comments
8. Field Review as needed
9. Wrap Up

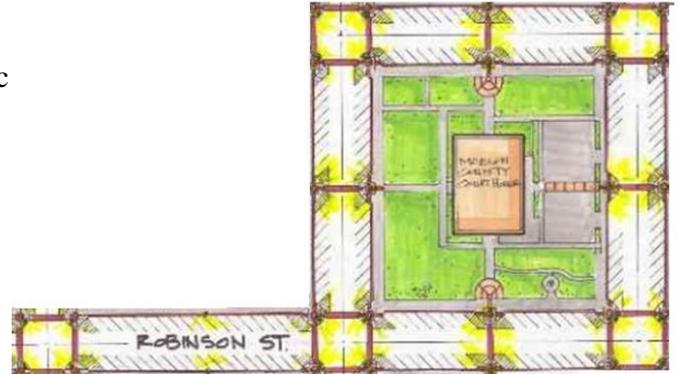

Work Completed to Date

Heavy rains were experienced last week.

April mentioned the nursery for the planters said we should check for 65 lbs on the arms. V&K Will follow up.

Water main is tied in at the intersection of 3rd and Robinson.

Subgrade is brought up to elevation. Testing occurred and passed before the rains last week. Proof rolling had issues on travel lanes. HP is re-compacting subgrade.

TK was on site one day last week. HP is trying to get them on site for other walks on 2nd Street.

If parking areas reach density, the need to proof roll these areas can be waived.

HP is hoping to get rock down before late week rains. Hopping paving will start immediately following rain.

Banner arms will be handled by City crews and staff.

VME should be getting on site between 2nd and 3rd. Footings will wait til parking is in.

HP is thinking that they may be paving the mainline of the street by month's end, weather depending.

Sidewalks on the Courthouse side will be 10 ft of PCC with 2 ft band making 12 ft total. This will occur on the N, W and S sides. Grass strip on east side will be eliminated.

Paving order is expected to be travel lanes first then parking. Footing for lights to follow with walks after.

The next meeting is **scheduled for Tuesday May 20th.**
