

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, June 17, 2014
10:00am




Present

The following is a summary of the discussions held during our progress meeting of the above date. The meeting was held at approximately 10 am in the Council Chamber at City Hall. The following agenda was generally followed. A sign in sheet was passed around and those present signed in. A copy of said sign-in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)
4. Expected work this next period
5. Questions
6. City's comments
7. Business/Property Owner comments
8. Field Review as needed
9. Wrap Up

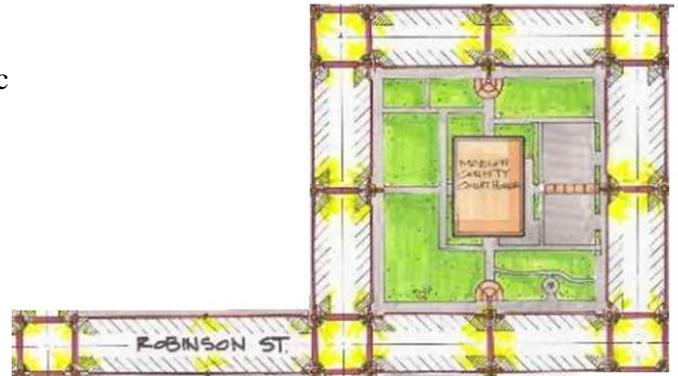

Work Completed to Date

Marion County Clocktower project is experiencing a major increase in work/costs and extension in time. Will need to coordinate longer with their contractor.

3rd and Main is closed and sewer flows being rerouted. 3rd and Robinson is open to traffic.

Remaining work on 2nd Street - sodding, pavers, crosswalks, joint sealing

Paver work is not occurring. Hawkeye Paving to contact, again.

Cal Stephens (Marion County) cited an issue concerning a person with a disability and issues in the rock. Skip and Hawkeye Paving will correct.

Work on 3rd to occur vigorously over the next several weeks. Water, storm, sanitary.

Greg Roth (V&K) and Brian Bailey (Knoxville Water Works) to layout new water main configuration for 2nd and Main and 1st and Robinson. Likely next project is two blocks west on Main St.

Greg to get an estimate together for the City.

Whether or not or where to continue work for this year following 3rd St was discussed. To be reviewed every meeting for the next several.

Alliant wants to cross 3rd at the appropriate time. Richard is in contact with them.

No full closures for paver work will be allowed.

The next meeting is **scheduled for Tuesday July 1.**
