

Downtown Streetscape Phase II Progress & Communication Meeting
Tuesday, July 15, 2014
10:00am




Present

The following is a summary of the discussions held during our progress meeting of the above date. The meeting was held at approximately 10 am in the Council Chamber at City Hall. The following agenda was generally followed. A sign in sheet was passed around and those present signed in. A copy of said sign-in is on file.

Agenda

1. Introductions
2. Sign In sheet
3. Work to date (since last meeting)

4. Expected work this next period
5. Questions
6. City's comments
7. Business/Property Owner comments
8. Field Review as needed
9. Wrap Up

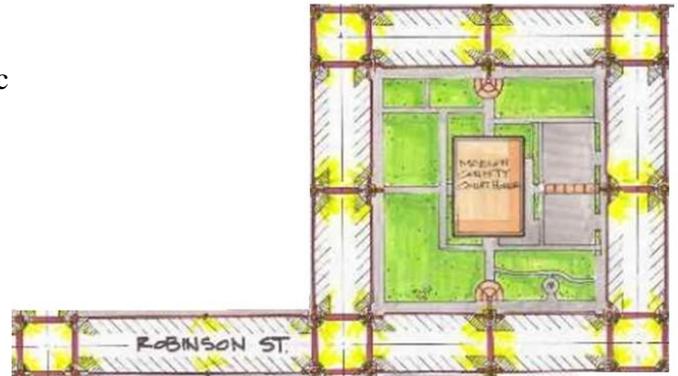

Work Completed to Date

Concrete pavers at the bumpouts will be placed this week. The Courthouse bumpouts will be a priority.

Sanitary sewer will be televised and inspected this week. Two sewer service laterals are left to install.

All underground work is expected to be complete by the end of July.

Van Maanen Electric will start install late this month. Fridays are good to install electrical on the Courthouse side since the tower contractor works 4 day work weeks.

Hardscape Solutions, Inc. (HSI) will need to power wash all stained pavers on site prior to sealing etc.

Hawkeye Paving is looking at starting the street paving August 1.

Stop signs are still in process of order.

Cal (Marion County Government) brought up that vendors at the Courthouse are getting tickets.

A walk through will be held with HSI after the meeting.

No full closures for paver work will be allowed.

The next meeting is **scheduled for Tuesday July 29.**
